

Mochi.dev

**MatchScore
Software Project Management Plan
Version *01.00***

<i>MatchScore</i>	Version: <i>01.00</i>
Software Requirements Specification	Date: <i>09/19/2026</i>
<i>SPMP</i>	

Revision History

Date	Version	Description	Author
09/19/2026	01.00	Initial Draft	John Michael B. Villamor

<i>MatchScore</i>	Version: <i>01.00</i>
Software Requirements Specification	Date: <i>09/19/2026</i>
<i>SPMP</i>	

Table of Contents

1	INTRODUCTION	4
1.1	PURPOSE OF PROJECT MANAGEMENT PLAN	4
2	EXECUTIVE SUMMARY OF PROJECT MANAGEMENT PLAN	4
2.1	ASSUMPTIONS/CONSTRAINTS	4
3	SCOPE MANAGEMENT	5
3.1	WORK BREAKDOWN STRUCTURE	5
3.2	DEPLOYMENT PLAN	5
3.3	CHANGE CONTROL MANAGEMENT	5
4	SCHEDULE/TIME MANAGEMENT	6
4.1	MILESTONES	6
4.2	PROJECT SCHEDULE	7
4.2.1	Dependencies	8
5	COST/BUDGET MANAGEMENT	8
6	QUALITY MANAGEMENT	8
7	HUMAN RESOURCE MANAGEMENT	8
8	COMMUNICATIONS MANAGEMENT	8
8.1	COMMUNICATION MATRIX	9
9	RISK MANAGEMENT	9
9.1	RISK LOG	9
10	ISSUE MANAGEMENT	9
10.1	ISSUE LOG	10
11	PROCUREMENT MANAGEMENT	10
12	COMPLIANCE RELATED PLANNING	10
	APPENDIX A: PROJECT MANAGEMENT PLAN APPROVAL	11
	APPENDIX B: REFERENCES	12
	APPENDIX C: KEY TERMS	13

MatchScore	Version: 01.00
Software Requirements Specification	Date: 09/19/2026
SPMP	

Software Project Management Plan

1 INTRODUCTION

1.1 PURPOSE OF PROJECT MANAGEMENT PLAN

The purpose of this Project Management Plan is to define how the MatchScore project will be planned, executed, monitored, and closed over its 9-week development period. It documents the scope, schedule, resources, risks, and communication approach that will guide the project.

The intended audience of the MatchScore PMP is all project stakeholders, including the course instructor and the project developer.

2 EXECUTIVE SUMMARY OF PROJECT MANAGEMENT PLAN

MatchScore is a web-based platform that allows job seekers to build a resume/portfolio, compare it against a job posting using a deterministic text-similarity algorithm (TF-IDF and cosine similarity), and receive AI-generated explanations and edit recommendations. This project will be developed by a single developer over a 9-week academic term, following an iterative build approach: document builder first, then the scoring engine, then the AI guidance layer.

2.1 ASSUMPTIONS/CONSTRAINTS

- The project will use a free-tier LLM API (e.g., Google Gemini or Groq); development is constrained by that API's rate limits.
- The developer has existing familiarity with React and Python/Flask, so minimal ramp-up time is budgeted.
- The MVP scope excludes a full portfolio-site builder and AI auto-edit; these are documented as stretch goals, given the compressed 9-week timeline.
- Development and testing will occur on the developer's personal machine; no dedicated staging/production server is budgeted.

MatchScore	Version: 01.00
Software Requirements Specification	Date: 09/19/2026
SPMP	

3 SCOPE MANAGEMENT

The scope of MatchScore is limited to the resume builder (templates, WYSIWYG editor, PDF import/export), the job-fit scoring engine (TF-IDF and cosine similarity), and the AI guidance layer (explanation and recommendations). Portfolio-site building, AI auto-edit, and job-posting URL scraping are out of scope for this 9-week delivery and documented as future work. Any request to expand scope will be evaluated against the remaining timeline per the Change Control Management process (Section 3.3) before being accepted.

3.1 WORK BREAKDOWN STRUCTURE

WBS Item	Description
1.0 Planning	Requirements gathering, SRS, SDD, SPMP documentation
2.0 Document Builder	Template system, WYSIWYG editor, PDF export, PDF import
3.0 Scoring Engine	Text preprocessing, TF-IDF vectorization, cosine similarity computation
4.0 AI Guidance Layer	Score explanation generation, recommendation generation
5.0 Integration & Testing	End-to-end testing of builder → scoring → AI guidance flow
6.0 Deployment & Demo Prep	Final deployment/hosting setup, demo rehearsal, documentation finalization

3.2 DEPLOYMENT PLAN

MatchScore will be deployed as a single web application accessible via browser. The deployment approach involves: (1) hosting the frontend (React) on a static hosting service, (2) hosting the backend (Flask/Express) on a free-tier cloud platform, (3) provisioning the database (SQLite for development), and (4) configuring the AI API key as a secured environment variable. No data conversion or legacy system integration is required, since this is a new, standalone application.

3.3 CHANGE CONTROL MANAGEMENT

Any proposed change to MatchScore's scope, schedule, or feature set will be documented and evaluated for impact on the remaining timeline before being approved. Given the compressed 9-week schedule, any change request received after Week 5 will default to being deferred to future work unless it directly addresses a blocking defect. Example: if the free-tier AI API's rate limits prove insufficient during development, a change may be required to increase caching of AI-generated content — this would be evaluated against the remaining schedule before implementation.

<i>MatchScore</i>	Version: <i>01.00</i>
Software Requirements Specification	Date: <i>09/19/2026</i>
<i>SPMP</i>	

4 SCHEDULE/TIME MANAGEMENT

The project schedule was baselined in Week 1 (current week) and will be reviewed weekly against actual progress. The developer is responsible for keeping the schedule updated and flagging any milestone at risk of slipping as early as possible, given the single-developer structure and the compressed 9-week timeline.

4.1 MILESTONES


The table below lists the milestones for this project, along with their estimated completion timeframe.

Milestones	Estimated Completion Timeframe
Requirements documentation complete (SRS, SDD, SPMP)	Week 1
Template system + WYSIWYG editor functional	Week 3
PDF export/import functional	Week 4
Scoring Engine (TF-IDF + cosine similarity) complete and tested	Week 5
AI Guidance Layer (explanation + recommendations) integrated	Week 6
Score history + remaining UI polish	Week 7
Full integration testing complete	Week 8
Final demo and submission	Week 9

MatchScore	Version: 01.00
Software Requirements Specification	Date: 09/19/2026
SPMP	

4.2 PROJECT SCHEDULE

<https://app.clickup.com/90161096109/v/li/901617685949>

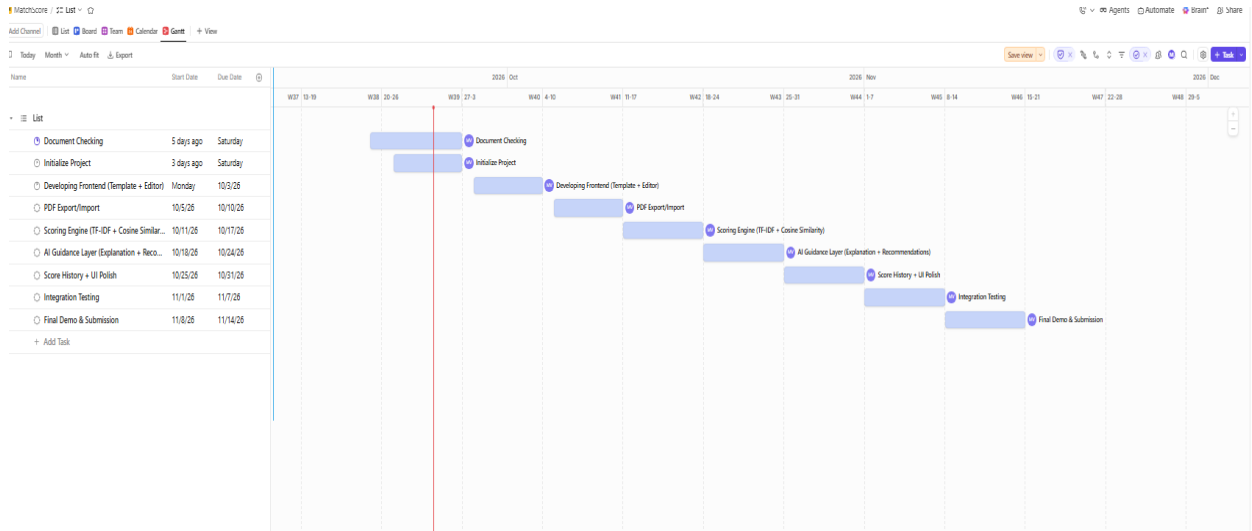

MatchScore / List					Agents Automate Brain ² Share
Add Channel List Board Team Calendar Gantt View					
Status					+ Task
IN PROGRESS 1					
Name	Assignee	Due date	Priority	Add	
Document Checking	MV	Sat, 7:30am	Urgent		
+ Add Task					
PLANNING 2					
Name	Assignee	Due date	Priority	Add	
Initialize Project	MV	Sat	High		
Developing Frontend (Template + Editor)	MV	10/3/26	High		
+ Add Task					
TO DO 6 ... +					
Name	Assignee	Due date	Priority	Add	
Scoring Engine (TF-IDF + Cosine Similarity)	MV	10/17/26	Normal		
AI Guidance Layer (Explanation + Recommendations)	MV	10/24/26	High		
Score History + UI Polish	MV	10/31/26	High		
Integration Testing	MV	11/7/26	High		
Final Demo & Submission	MV	11/14/26	Normal		
PDF Export/Import	MV	10/10/26	High		
+ Add Task					

MatchScore	Version: 01.00
Software Requirements Specification	Date: 09/19/2026
SPMP	

4.2.1 Dependencies

- The AI Guidance Layer (Week 6) depends on the Scoring Engine (Week 5) being complete, since AI explanations require a computed score as input.
- Integration testing (Week 8) depends on all prior milestones being functionally complete.
- Final demo prep (Week 9) depends on integration testing passing without blocking defects.
- External dependency: continued availability of the chosen free-tier AI API within its published rate limits, throughout Weeks 5–9.

5 COST/BUDGET MANAGEMENT

As a solo academic project, MatchScore has no monetary budget beyond optional hosting costs, expected to remain within free tiers (frontend hosting, backend hosting, and the AI API). No paid services are planned; if a paid tier becomes necessary, this will be raised as a change per Section 3.3.

6 QUALITY MANAGEMENT

Quality will be maintained through: (1) manual testing of each feature against its corresponding requirement in the SRS before it is considered complete, (2) verification that the match-score algorithm produces consistent, reproducible results for the same input pair, (3) review of AI-generated explanations and recommendations for relevance and adherence to the constraint that auto-edit never fabricates new claims, and (4) a defect log tracking any bugs found during testing until resolved and re-verified. Given the 9-week timeline, testing is scheduled as a dedicated activity in Week 8 rather than left until the final days before submission.

7 HUMAN RESOURCE MANAGEMENT

This project is developed by a single team member, who is responsible for all roles: requirements analysis, design, frontend development, backend development, AI integration, testing, and documentation.

8 COMMUNICATIONS MANAGEMENT

As a solo project, most communication is between the developer and the course instructor. Progress updates will be shared according to the course's required check-in schedule.

<i>MatchScore</i>	Version: <i>01.00</i>
Software Requirements Specification	Date: <i>09/19/2026</i>
<i>SPMP</i>	

8.1 COMMUNICATION MATRIX

Stakeholder	Messages	Vehicles	Frequency	Communicators	Feedback Mechanisms
Instructor	Progress updates, milestone deliverables	Email / LMS submission	Weekly (per milestone)	Developer	Instructor feedback/grading comments
Developer (self)	Task progress, blockers	Personal task tracker	Ongoing	Developer	Self-review against 9-week schedule

9 RISK MANAGEMENT

Risks will be identified as they arise and logged with a description, likelihood, impact, and mitigation plan. Given the compressed 9-week timeline, schedule risk is treated as the highest-priority category.

9.1 RISK LOG

Risk	Likelihood	Impact	Mitigation
Document Builder (Weeks 2–4) slips, delaying everything after it	Medium	High	Treat Weeks 2–4 as the highest-priority window; cut portfolio-site stretch scope immediately if behind
Free-tier AI API rate limit hit during development or demo	Medium	High	Cache AI responses per resume/job-posting pair; pre-test demo flow ahead of time
PDF parsing fails on inconsistently formatted resumes	Medium	Medium	Support plain text input as a fallback; test with multiple sample PDFs early (Week 4)
Insufficient time left for integration testing	Medium	High	Keep Week 8 reserved exclusively for testing; do not let feature work bleed into it
AI Auto-Edit or portfolio-site scope creep delays MVP	Medium	Medium	Both are explicitly out of scope for the 9-week MVP (Section 3)

10 ISSUE MANAGEMENT

Issues (realized problems, as opposed to risks) will be logged with a description, date identified, and resolution status, and tracked until closed.

<i>MatchScore</i>	Version: <i>01.00</i>
Software Requirements Specification	Date: <i>09/19/2026</i>
<i>SPMP</i>	

10.1 ISSUE LOG

Maintained separately as a running log during development [insert link or reference here, e.g., a GitHub Issues board or spreadsheet].

11 PROCUREMENT MANAGEMENT

No procurement is required for this project. All tools used (React, Flask/Express, SQLite, free-tier AI API, hosting platforms) are free and self-provisioned by the developer.

12 COMPLIANCE RELATED PLANNING


MatchScore will avoid storing any sensitive personal data beyond what the user voluntarily enters into their resume, and will not share user resumes or job postings with third parties outside the AI API call required to generate explanations/recommendations. No additional regulatory compliance (e.g., HIPAA, FERPA) applies to this project's scope.

<i>MatchScore</i>	Version: <i>01.00</i>
Software Requirements Specification	Date: <i>09/19/2026</i>
<i>SPMP</i>	

APPENDIX A: PROJECT MANAGEMENT PLAN APPROVAL

The undersigned acknowledge they have reviewed the ***MatchScore* Project Management Plan** and agree with the approach it presents. Changes to this **Project Management Plan** will be coordinated with and approved by the undersigned or their designated representatives.

Signature:



Date: 09/24/26

Print Name:

JOHN MICHAEL B. VILLAMOR

Title:

AI Enthusiast

Role:

Full Stack Developer

Signature:

Date: _____

Print Name:

Title:

Role:

Signature:

Date: _____

Print Name:

Title:

Role:

<i>MatchScore</i>	Version: <i>01.00</i>
Software Requirements Specification	Date: <i>09/19/2026</i>
<i>SPMP</i>	

APPENDIX B: REFERENCES

The following table summarizes the documents referenced in this document.

Document Name and Version	Description	Location
MatchScore SRS v01.00	Software Requirements Specification	MS Teams Shared Files
MatchScore SDD v01.00	Software Design Document	MS Teams Shared Files

<i>MatchScore</i>	Version: <i>01.00</i>
Software Requirements Specification	Date: <i>09/19/2026</i>
<i>SPMP</i>	

APPENDIX C: KEY TERMS

The following table provides definitions for terms relevant to this document.

Term	Definition
TF-IDF	Term Frequency–Inverse Document Frequency, a text-weighting technique
Cosine Similarity	A measure of similarity between two text vectors
MVP	Minimum Viable Product
WBS	Work Breakdown Structure
